




INTERNATIONAL TREASURE GROUP LLC

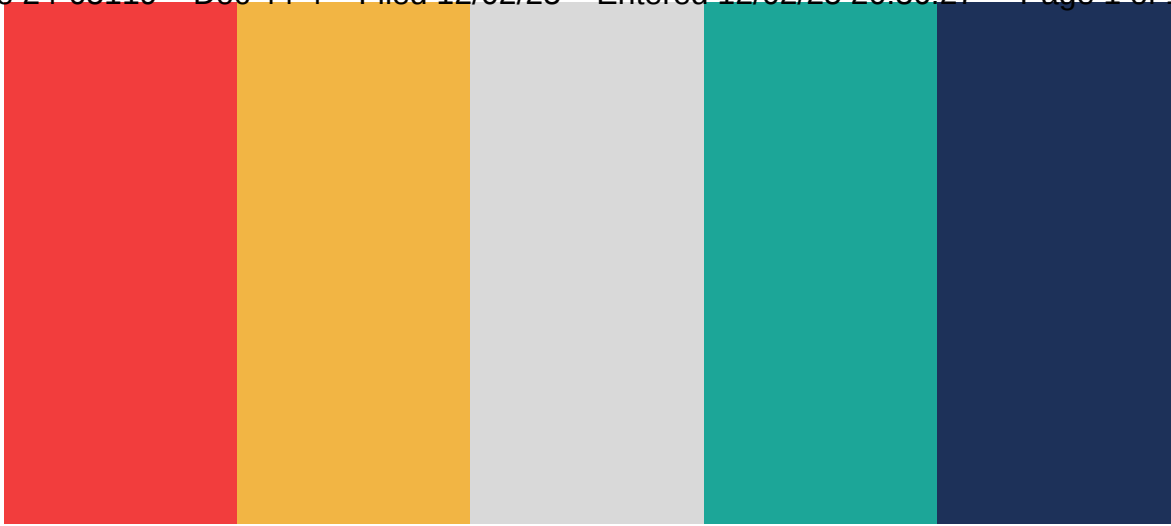

BRAZIL LARGE-SCALE LAUNCH
CONSULTING / ADVISORY PROPOSAL

Paulo Figueiredo Filho
Managing Partner

August 16th, 2021





Table of Contents

Background..... 2

 Main Objectives..... 2

 Project Summary..... 2

Leadership 3

 Marcelo de Paulos..... 3

 Paulo Figueiredo Filho 4

Proposal..... 5

 I. Strategic Planning 5

 II. Setup of Operations..... 9

 III. Launch 12

 IV. Advisory..... 14

Pricing and Terms & Conditions 15

 Duration..... 15

 Pricing 15

 Terms & Conditions 15





Background

GETTR is a social media platform that intends to fill in a gap created by the widespread suppression of conservative voices by Big Tech, starting in the USA but with effect in many other countries around the globe.

Given the current vitality of the conservative movement in Brazil, the country corresponds to nearly 15% of GETTR's usage.

Jason Miller, GETTR's CEO, has plan to set up shop in Brazil and capitalize on the spontaneous growth the platform has seen in the country so far. Although the platform already garners a sizeable usage in the country, it appears that a locally-run operation, along with an appropriate market launch, will accelerate growth in considerable fashion.

Doing business in Brazil has very particular intricacies. In the common vernacular, it is said that "Brazil is not for amateurs," implying that it takes someone with deep knowledge of the culture, the legal system, the politics, the customs and the norms in order to succeed in the country.

Main Objectives

The purpose of this consultancy is to offer the necessary guidance for GETTR not only to avoid common pitfalls of the Brazilian business and political landscape, but also to help it thrive in and from it.

Project Summary

This project intend to cover GETTR's needs over the remaining months of the calendar year of 2021, comprising the following phases:

- I. **Strategic Planning**
- II. **Setup of Operations**
- III. **Launch**
- IV. **Advisory**

Leadership

Marcelo de Paulos



Marcelo has built a solid career in Media and Marketing, particularly in the digital space.

After graduating in Social Communication from the Federal University of Rio de Janeiro, he worked for top Direct Marketing and Branding agencies and companies in Insurance, Telecom and Ecommerce, before becoming the Marketing Director at Unibanco, one of the top retail banks in the country (later merged with Itaú to

become the largest bank in the Southern Hemisphere).

In 2010, Marcelo got his Master's degree in Business from Stanford University, where he did research work on Brazil's soccer business. He returned to Brazil to become the first General Manager of 9ine, a sports marketing agency owned by soccer legend Ronaldo and the WPP Group and later ventured in two sports startups before moving back to the corporate world. He also advised two members of the Moreira Salles family (shareholders of Itaú Unibanco) in their investments at Botafogo, a top tier soccer club in Rio.

Marcelo helped Yahoo Brazil transition to a player in the programmatic advertising world and later became Director of Digital Strategies at Estadão, one of the top newspapers in the country – where he established a well-oiled machine of digital subscriptions that broke records.

Marcelo recently joined Hotmart, the world's top end-to-end platform for digital products (mainly online courses), which recently broke the US\$ 1 billion valuation mark. He will perform as the scale-up's Global Head of Growth.

Paulo Figueiredo Filho



Paulo has a very unusual set of skills, having achieved international success in several areas.

He studied Social Communication and Economics at the Pontifical Catholic University of Rio de Janeiro, one of the most respected universities in Latin America. Later, he joined programs at renowned international universities such as a Micromasters in Microeconomics at MIT, Negotiation Mastery at Harvard Business School and Business, International Relations & Political Economy at the


London School of Economics and Political Science.

Paulo had an expressive experience in the public sector, having served as national congressman staff member, special advisor, and chief of staff in the State Government and the City Hall of Rio de Janeiro.

As an entrepreneur, he led multimillion-dollar corporations in the Real Estate, entertainment, e-commerce, and hospitality sectors in the Brazilian, North American, and Chinese markets. Among his most important projects is the development of what was the Trump Hotel Rio de Janeiro.

As a journalist, Paulo Figueiredo has become one of Brazil's most respected political commentators, being considered the country's foremost authority on American politics. He worked as a political commentator for Grupo Jovem Pan (the largest radio/tv group in Brazil) and is currently contributes to the newspaper Gazeta do Povo and co-host a show at Terça Livre, the largest independent media outlet in Latin America.

On his social networks, Paulo has hundreds of thousands of faithful followers across multiple platforms.



Proposal

I. Strategic Planning

What it comprises of

Detailed guidance on decisions that predate the Setup of Operations and the actual large-scale Launch, divided into the following four subjects:

1. Legal Counsel

- **Scope**
 - Procurement and referral of ideal law firm/s to assist GETTR in setting up the Brazil operation.
 - Interface with the law firm/s to assist GETTR in the definition on a number of essential topics for the future operation, which includes (non-exhaustive list):
 - (*URGENT ITEM*) Production of Terms of Service and Terms & Conditions for the platform, in Portuguese and in compliance with the local laws and regulations.
 - (*URGENT ITEM*) Production of a strategy and a response process for judicial demands.
 - Ideal setup of legal entities, especially in relation to the US/Global structure.
 - Guidelines for Corporate, Tax and Labor law compliance.
 - Compliance with local laws and regulations that govern the activity of social network services (privacy/data protection, civil, criminal, consumer and internet governance).
 - Drafting of a Policy/Government Relations strategy.
 - Recommendations on the legal and aspects of the decision as to which functions of the business to place in Brazil and which to be performed abroad.
- **What Triggers This Task**
 - Approval of this proposal.
- **Steps and Expected Timeframes:**
 - Attending to Urgent Items.
→ *Week 1-2*
 - Comprehensively understanding GETTR's business needs.
→ *Week 1*
 - Producing the exhaustive list of legal topics that are essential to the proper launch of services in the country. (GETTR's relationship with the law firm[s] might go beyond the scope of this proposal in both scope and time.)
→ *Week 1-2*
 - Procuring and referring the ideal law firm/s.
→ *Week 2-3*
 - Interfacing with the law firm/s until the delivery of all the recommendations

→ *Dependent upon breadth of list, GETTR's team engagement and delivery time of law firm.*

- **Deliverables**

- Written recommendation of law firm/s with rationale based on the understanding of GETTR's business needs, which will be part of the same document.
- Written advice by this consultancy if input additional to the law firm's recommendation is in order and requested.

week→	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
STRATEGIC PLANNING																				
Legal Counsel																				
<i>Timeframe triggered by: Acceptance of Proposal</i>																				
Attending to Urgent Items																				
Understanding of Needs																				
Production of Essentials List																				
Procurement and Referral of Law Firm																				
Interfacing with Law Firm																				
Deliverable: Referral of Law Firm																				
Deliverable: Ad Hoc Advice																				

2. Localization of operations

- **Scope**

- Recommendations in regards to the local operation of GETTR as to when, what and how to set up within Brazil's borders – which might include the creation of legal entities, the nomination of local legal proxies, the setting up of a local office and the hiring of a Country Manager.

- **What Triggers This Task**

- Initial meeting hosted by GETTR.

- **Steps and Expected Timeframe**

- Understanding the implications (legal, financial, operational, labor, commercial, technological and practical) of GETTR's operation.

→ *Week 1*

- Providing thorough recommendations, which weigh out pros and cons of every implication assessed.

→ *Week 2-3*

- **Deliverables**

- Written recommendations.

week→	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
STRATEGIC PLANNING																				
Localization of Operations																				
<i>Timeframe triggered by: Initial Meeting Hosted by GETTR</i>																				
Understanding Implications																				
Providing Recommendations																				
Deliverable: Recommendations																				

3. Establishment of the Brand

- **Scope**
 - Guidance on the strategic aspects of the GETTR brand in Brazil: market positioning, branding strategy, advertising campaigns, customer acquisition principles.
 - Guidance on the basic PR strategy and referral of PR firm to lead it.
 - Hiring and supervising Advertising agency/ies to lead the launch and the customer acquisition campaigns.
- **What Triggers This Task**
 - Initial meeting hosted by GETTR.
- **Steps and Expected Timeframe**
 - Understanding GETTR's overarching branding strategy, market positioning, current advertising and customer acquisition practices.
→ *Week 2*
 - Procurement and referral of ideal PR firm and Advertising agency/ies.
→ *Week 3-4*
 - Briefing PR firm for the layout of the PR strategy.
→ *Week 4*
- **Deliverable**
 - Written report with the recommendations encompassed in the scope.

week→	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
STRATEGIC PLANNING																				
Establishment of the Brand																				
<i>Timeframe triggered by: Initial Meeting Hosted by GETTR</i>																				
Understanding Branding Strategy																				
Procurement/Referral PR + Ad Agency																				
Briefing PR Firm																				
Deliverable: Recommendations																				

4. Traffic Generation Drivers

- **Scope**
 - Recommendation of strategies with the goal of speeding up growth of user base and usage of GETTR in Brazil, along with the adequate approach in order to attract their engagement with the platform.
 - Influencers might fall into one of the following categories:
 - Individuals (politics-related): digital influencers, meme artists, comedians.
 - Media Outlets: legacy (print, radio, TV) and digital (portals, blogs, successful social media profiles, commentators).
 - Political Actors: politicians, political leaders, government officials, activists, political organizations.
 - Beyond Politics: influencers with large following in topics such as sports, entertainment, behavior, fashion and lifestyle, among others.
- **What Triggers This Task**
 - Initial meeting hosted by GETTR.

- **Steps and Expected Timeframe**

- Understanding GETTR's current strategy in other markets.
→ *Week 1-2*
- Assessment of who already is on GETTR and the level of their engagement with the platform's users.
→ *Week 1-2*
- Developing the overarching growth strategy.
→ *Week 2-3*
- Plotting influencers in each category that fit the strategy.
→ *Week 3-4*
- Laying out the proposal with which to approach the individual influencers.
→ *Week 3-4 on*

- **Deliverables**

- Written recommendation of overarching growth strategy.
- Written list of influencers to be approached and the recommended proposal for each.

week→	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
STRATEGIC PLANNING																				
Traffic Generation Drivers																				
<i>Timeframe triggered by: Initial Meeting Hosted by GETTR</i>																				
Understanding Growth Strategy																				
Local Assessment of Current Influencers																				
Developing Overarching Local Strategy																				
Plotting Influencers																				
Laying Out Proposals																				
Deliverable: Growth Strategy																				
Deliverable: List of Influencers																				

II. Setup of Operations

What it comprises of

Subject to the recommendations in the Strategic Planning phase, two scenarios may be contemplated at this time:

- **Remote:** Maintaining the bulk of the operation in the US and setting up local assistance with the hiring of vendors, contractors and legal proxies until local legal entities are unavoidable.
- **Local:** Setting up local legal entities and full operation (office, team).

The scope of this phase includes initiatives that might take place under any of the scenarios listed above within the calendar year of 2021.

1. Establishment of Processes That Allow For Hiring and Compensating Service Providers

- **Scope**
 - Recognizing the need, procuring and referral of vendors such as (non-exhaustive list):
 - Accounting firm
 - Marketing and communication service providers.
 - Influencers and their eventual agents
 - IT/Tech Infrastructure providers
- **What Triggers This Task**
 - Initial meeting hosted by GETTR.
- **Steps and Expected Timeframes**
 - Recognizing the need (generated by the GETTR team, this consultancy or any of the hired vendors) for a particular service provider.
→ *Inception of task*
 - Providing a short list of referral for potential vendors.
→ *2 weeks*
 - Interfacing with selected vendor to forward hiring.
→ *2 weeks*
- **Deliverables**
 - Written referral of shortlist of vendors for each recognized need.

week→	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
SETUP OF OPERATIONS																				
Service Providers Process																				
<i>Timeframe triggered by: Initial Meeting Hosted by GETTR (for each individual need)</i>																				
Recognizing the Need																				
Providing Shortlist																				
Interface With Service Provider																				
Deliverable: Referrals																				

2. Opening Up the Local Office

- **Scope**
 - Assistance opening up the physical local office.
- **What Triggers This Task**
 - Initial meeting hosted by GETTR.
- **Steps and Expected Timeframes (after final decision is made)**
 - Procurement and referral of real estate firm/agent to find, refer and sign the office location.
→ *2 weeks*
 - Procurement and referral of office design, renovation and facilities contractors.
→ *2-3 weeks*
 - Interfacing with service providers in order to maximize output.
→ *Dependent on service providers' timeframe*
- **Deliverables**
 - Written advice by this consultancy if input additional to the real estate firm's recommendation is in order and requested.

week→	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
SETUP OF OPERATIONS																				
Opening Up Local Office																				
<i>Timeframe triggered by: Initial Meeting Hosted by GETTR (for each individual need)</i>																				
Procuring and Referring of RE Agent																				
Procuring and Referring of Other Service Providers																				
Deliverable: Referral RE Agent																				
Deliverable: Referral Other Service Providers																				

3. Hiring the Local Leadership

- **Scope**
 - Assistance hiring the local startup team. (In principle, this team might relieve this consultancy of its operational duties. In this case, this consultancy will then perform solely as advisors.)
- **What Triggers This Task**
 - Definition on the positions to be filled.
- **Steps and Expected Timeframes (after final decision is made)**
 - Procuring and referring an Executive Search firm
→ *2 weeks*
 - Assistance in briefing the firm on the profiles of the startup team positions
→ *2 weeks, subject to the definitions by the GETTR's team*
 - Assistance in selecting the best candidates
→ *Compliant to the interviewing and selection process*

- Deliverables

- Recommendation of Executive Search firm.
- Written advice by this consultancy if input additional to the Executive Search firm is requested.

week→	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
SETUP OF OPERATIONS																				
Hiring the Local Leadership																				
<i>Timeframe triggered by: Definition on the Positions to Be Filled</i>																				
Defining Positions																				
Procuring and Referring Executive Search Firm																				
Briefing the Executive Search Firm																				
Assistance in Selection																				
Deliverable: Referral Executive Search Firm																				
Deliverable: Ad Hoc Advice																				

III. Launch

What it comprises of

Coordination of the most strategic aspects of the large-scale launch of GETTR in Brazil.

1. Marketing and Communication

- **Scope**
 - Assistance in the conception and execution of the initiatives involved in the proper launch of GETTR to the general public in Brazil.
 - Supervision of the PR firm's work.
 - Assistance in the briefing and approval steps of the advertising campaigns.
- **What Triggers This Task**
 - Deliverable of task "Strategic Planning (3) Establishment of the Brand" approved.
- **Steps and Expected Timeframes**
 - Supervision of PR
→ *Ongoing*
 - Assistance in briefing advertising agency
→ *1 week after agency's hiring*
 - Assistance in approval of advertising campaigns
→ *Compliant with advertising agency's schedule*
- **Deliverables**
 - Report on PR firm, if and when requested
 - Written documents pertaining to the advertising agency's briefing

week→	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
LAUNCH																				
Marketing and Communication																				
<i>Timeframe triggered by: Approval of "Establishment of the Brand" deliverable</i>																				
Supervision of PR																				
Briefing Advertising Agency																				
Approval of Advertising Campaigns																				
Deliverable: Ad Hoc Report on PR																				
Deliverable: Agency Brief																				

2. Influencers

- **Scope**
 - Assistance in executing the strategy laid out to attract of the desired influencers in each category:
 - Individuals
 - Media Outlets
 - Political Actors
 - Beyond Politics
- **What Triggers This Task**
 - Deliverable of task “Strategic Planning (4) Traffic Generation Drivers” approved.
- **Steps and Expected Timeframes**
 - Procurement and referral of a service provider/s to execute the attraction strategy.
→ *2-3 weeks*
 - Assistance on the implementation of eventual programs aimed at Media Outlets.
→ *4-6 weeks*
 - Introductions to key influencers, when needed and applicable – expected to be applicable to Political Actors.
→ *When opportunity arises*
- **Deliverables**
 - Written report on the work of the service provider, as per request.


week→	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
LAUNCH																				
Influencers																				
<i>Timeframe triggered by: Approval of "Traffic Generation Drivers" deliverable</i>																				
Procuring and Referring Service Provider																				
Assistance on Implementing Program (Media Outlets)																				
Introduction to Key Influencers																				
Deliverable: Ad Hoc Report on Service Provider																				

IV. Advisory

After GETTR's local leadership is assigned, this consultancy assumes an advisory role.

- **Scope**
 - Based on information provided by GETTR's team, provide a local, detached stance on the performance of the platform, the leadership and key service providers.
 - Advising on key strategic moves, as per GETTR's request.
- **Steps and Expected Timeframes**
 - Periodic reviews.
→ *Monthly*
 - Ad Hoc informed opinion on particular issues.
→ *Whenever necessary*
- **Deliverables**
 - Written monthly reviews.
 - Written recommendation/advice on Ad Hoc requests

week→	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
ADVISORY																				
<i>Timeframe triggered by: Hiring of Local Leadership</i>																				
Periodic Reviews																				
Ad Hoc Opinion																				
Deliverable: Monthly Reviews																				
Deliverable: Ad Hoc Report																				



Pricing and Terms & Conditions

Duration

This consultancy comprises the remaining months of the calendar year of 2021.

- By November 30, 2021, GETTR and this consultancy will reach a new agreement pertaining any period beyond 2021.

Pricing

Nature	Value	Due Date
Monthly Retainer	US\$ 35,000	Every 5th of the month, starting Aug 5, 2021

Terms & Conditions

- The amounts described in the Pricing section cover the services rendered by the Leadership of International Treasure Group LLC (ITG) listed in this proposal.
 - The cost of additional personnel eventually necessary for the rendering of services in this proposal will be added to the respective total amount, subject to approval of GETTR prior to the hiring of such personnel.
 - Additional expenses incurred by ITG will be reimbursed by GETTR, subject to approval prior to realization of such expenses.
 - Services to be rendered by third parties (such as law, accounting, PR, advertising firms) are not covered by this proposal's fees and will be billed directly to GETTR or its due legal proxy.
 - Services not requested by GETTR or to which GETTR eventually fails to provide necessary information, authorization or approval might not be rendered. These services not rendered do not grant GETTR with any rights to reduction in price or future credit in services.
- This consultancy is responsible for recommendations that fall into its purview.
 - Any expert advice provided by other service provider or individual, even if as a consequence of the scope of this current project, are the sole responsibility of the respective service provider.
- The ultimate legal responsibility and liability of the implementation of the direct product of this consultancy relies entirely upon GETTR.
- In the event that any demand exceed the scope of the current proposal, ITG and GETTR will negotiate as to whether the additional service will incur any extra fees.
 - If both parties agree on such incurrence, ITG will promptly send a quote of the extra fee for approval by GETTR.

- All payments will be made in US dollars, to ITG's legal entity in the USA.

Approval:

Jason Miller
GETTR - CEO
